CASE STUDY GCA SANDON DOCK






RESTRICTIONS



- Multi contractor site with no lay down areas
- Limited site road access round construction areas
- No out of hours working permitted



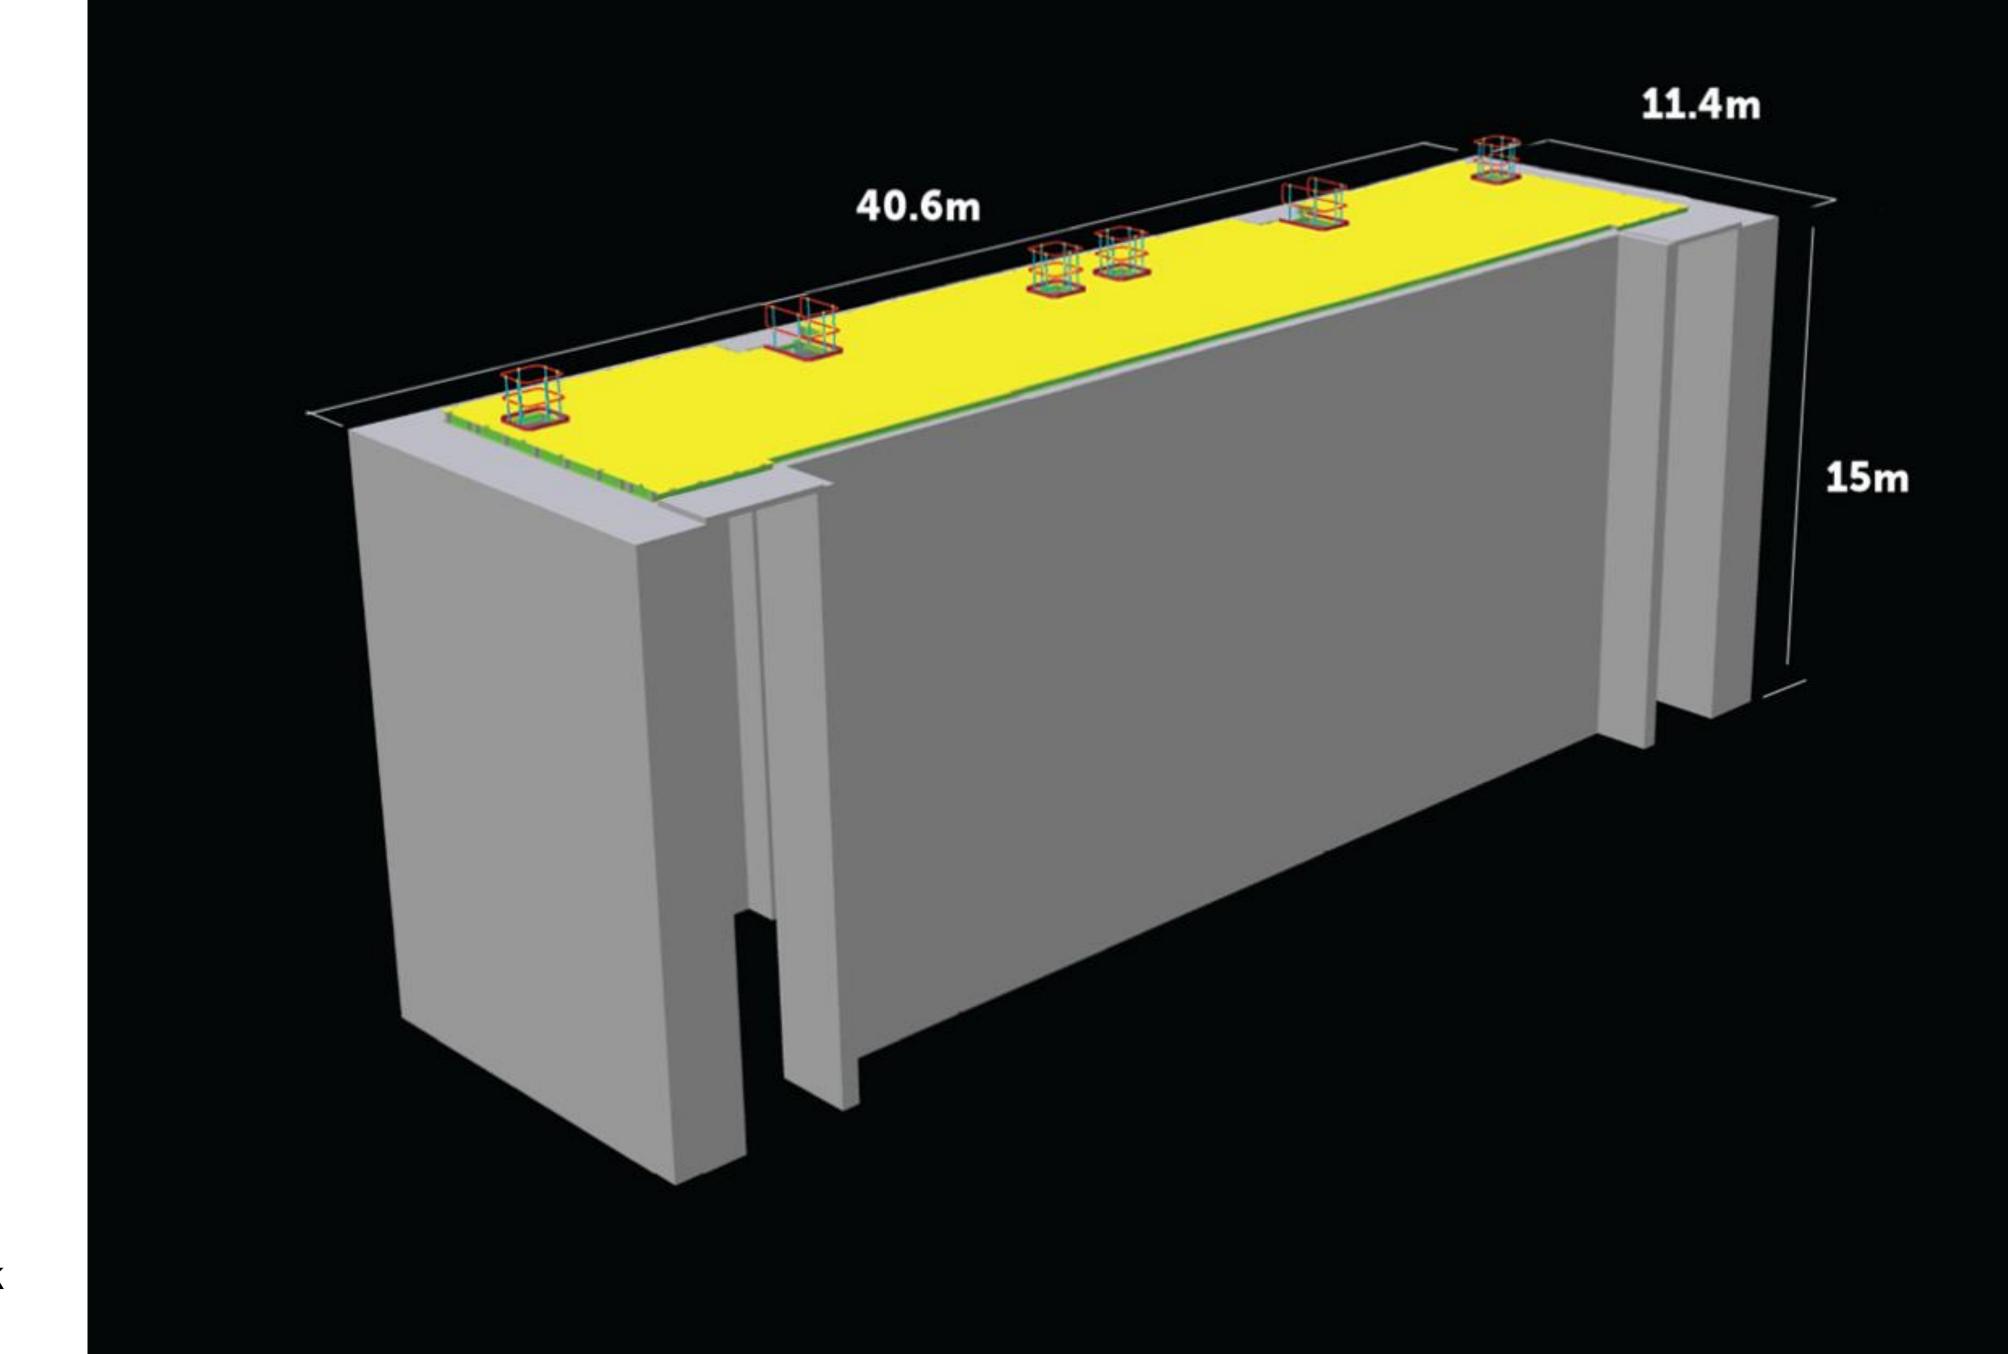
















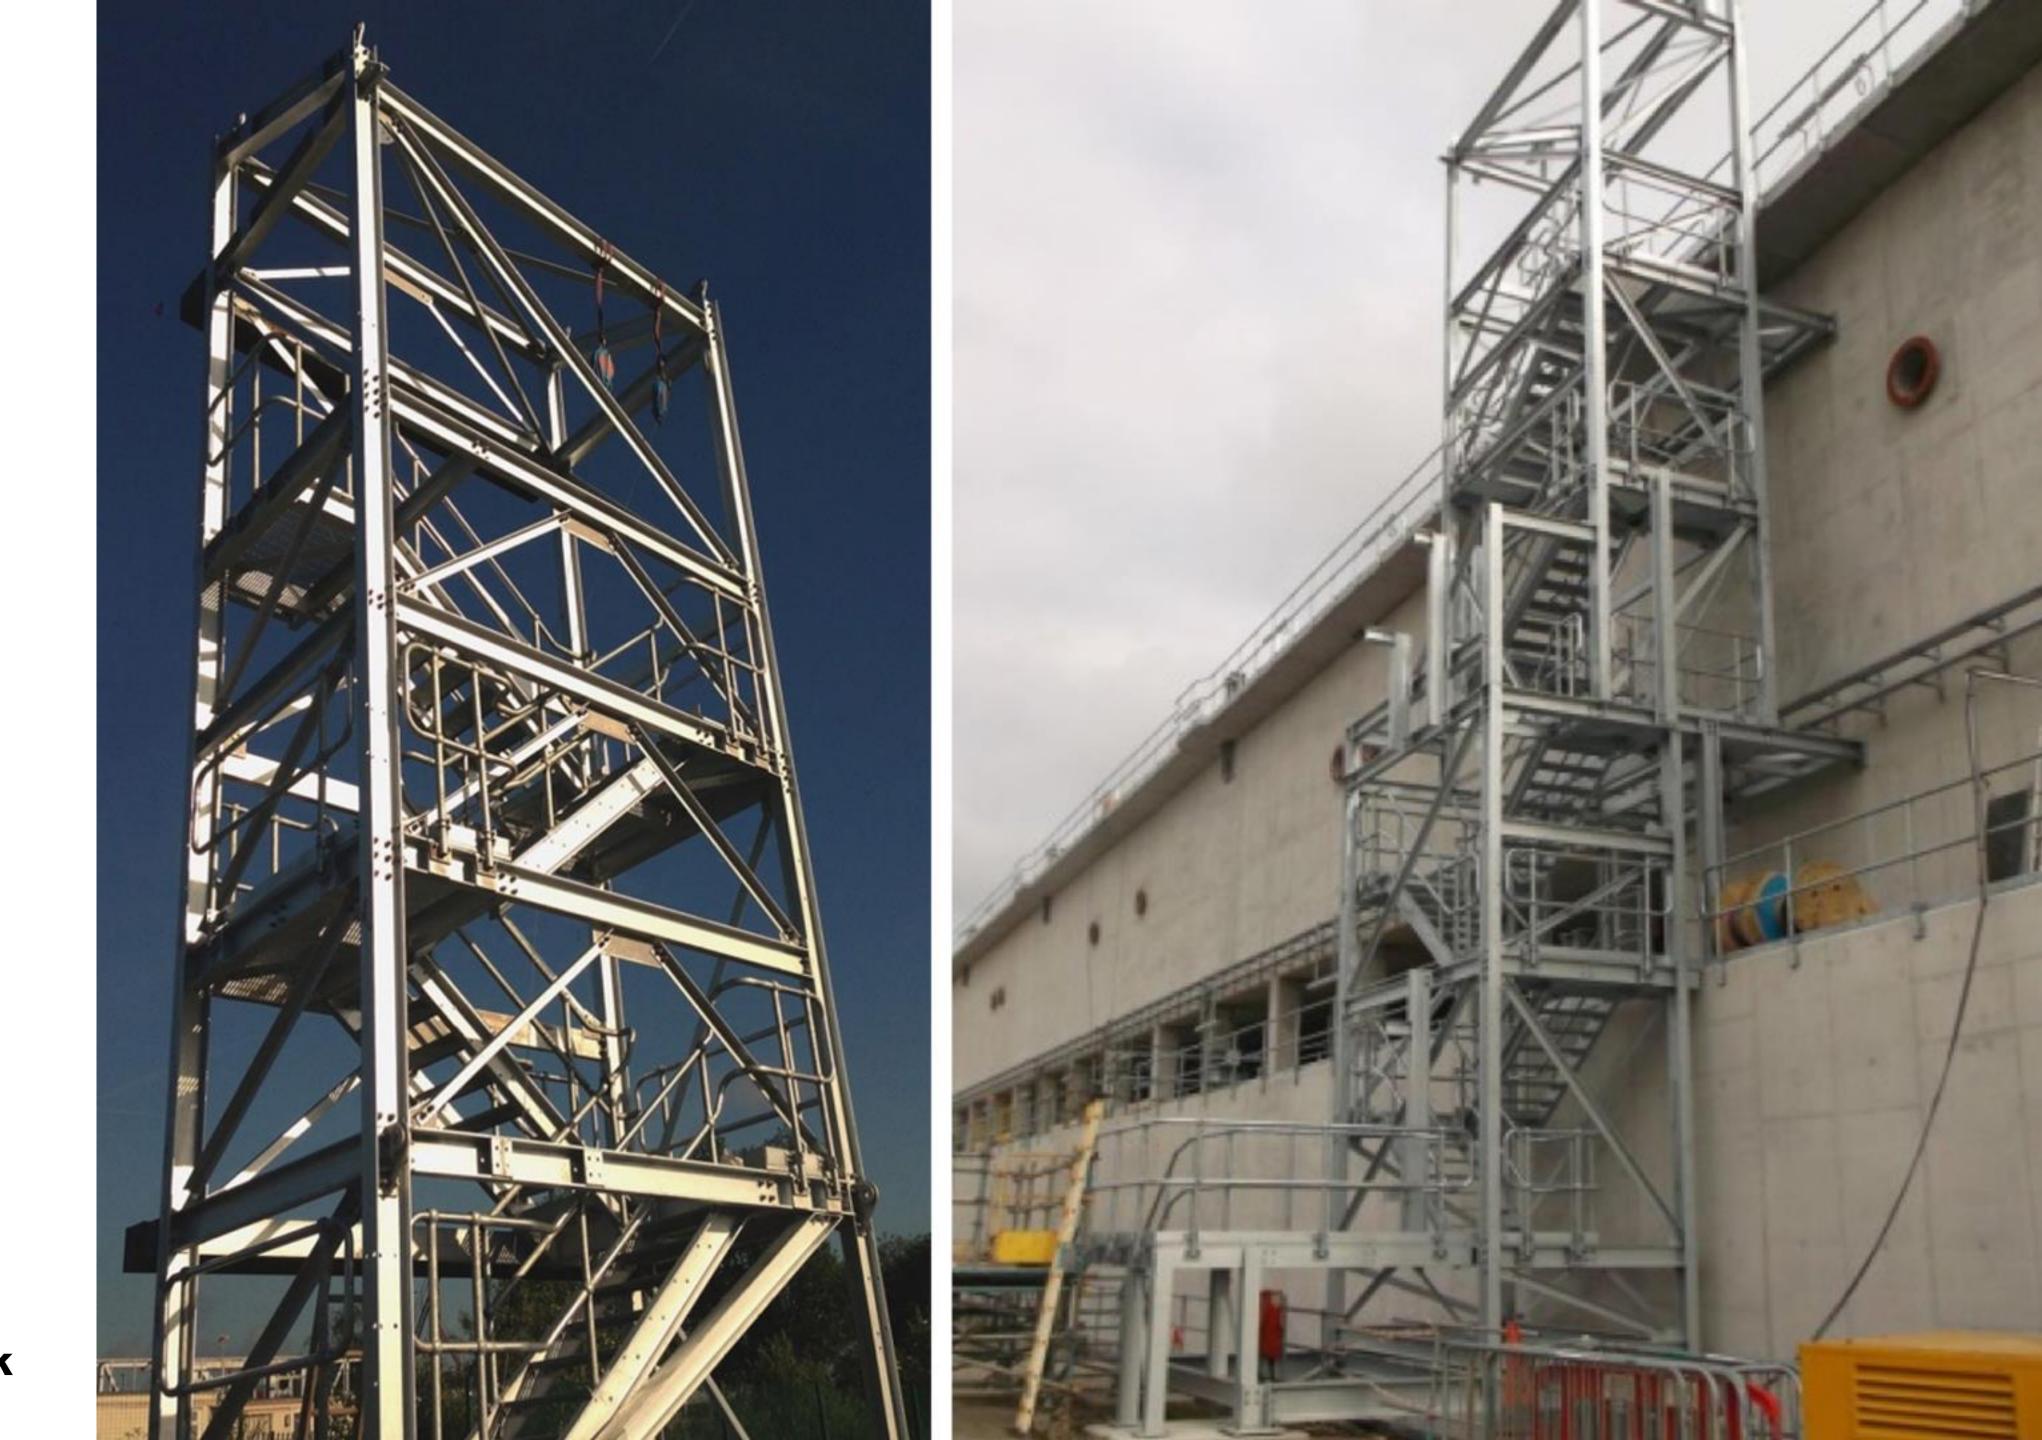





IMPACT OF MODULAR CONSTRUCTION



- decanter) **19 weeks on site saving**
- 6 weeks on site saving
- £125k saving to client

Installation time reduced from 3 weeks to 3 days x 8 (per

Onsite time reduced from 24 weeks to 5 weeks

 Staircases installation reduced from 2 weeks to 2 days x 4 Onsite time reduced from 8 weeks to 2 weeks

Overall cost of prelims on site 25 weeks saved

BENEFITS OF MODULAR CONSTRUCTION



- Modules constructed off site safely and quickly
- Multiple modules delivered at once
- Quick and efficient testing
- Early communication with multiple specialists
- Efficient working

